



Improving mobility

Easing congestion

Strengthening our communities

Central Corridor **Light Rail Transit**



# Transportation Committee

October 22, 2012



Improving mobility

Easing congestion

Strengthening our communities

Central Corridor **Light Rail Transit**



# 2013 Contract Amendment for AECOM Engineering

## 2012-324

# Background

## Central Corridor Light Rail Transit



- Contract executed June 2007
- Amendments executed for 2011 and 2012 to cover Design Support During Construction and Construction support
- Amendments for 2011, 2012 and 2013 were anticipated costs and are covered by Project Contingency


# Background

## Central Corridor Light Rail Transit



- AECOM responsibilities
  - Preliminary Engineering - **Completed**
  - Final Design - **Completed**
  - Design Support during Construction – **In Progress**
  - Construction Support – **In Progress**
  - Light Rail Vehicle Support Services - **In Progress**
  - System Integration Testing Support Services - **In Progress**

# Construction Complete through August 2012

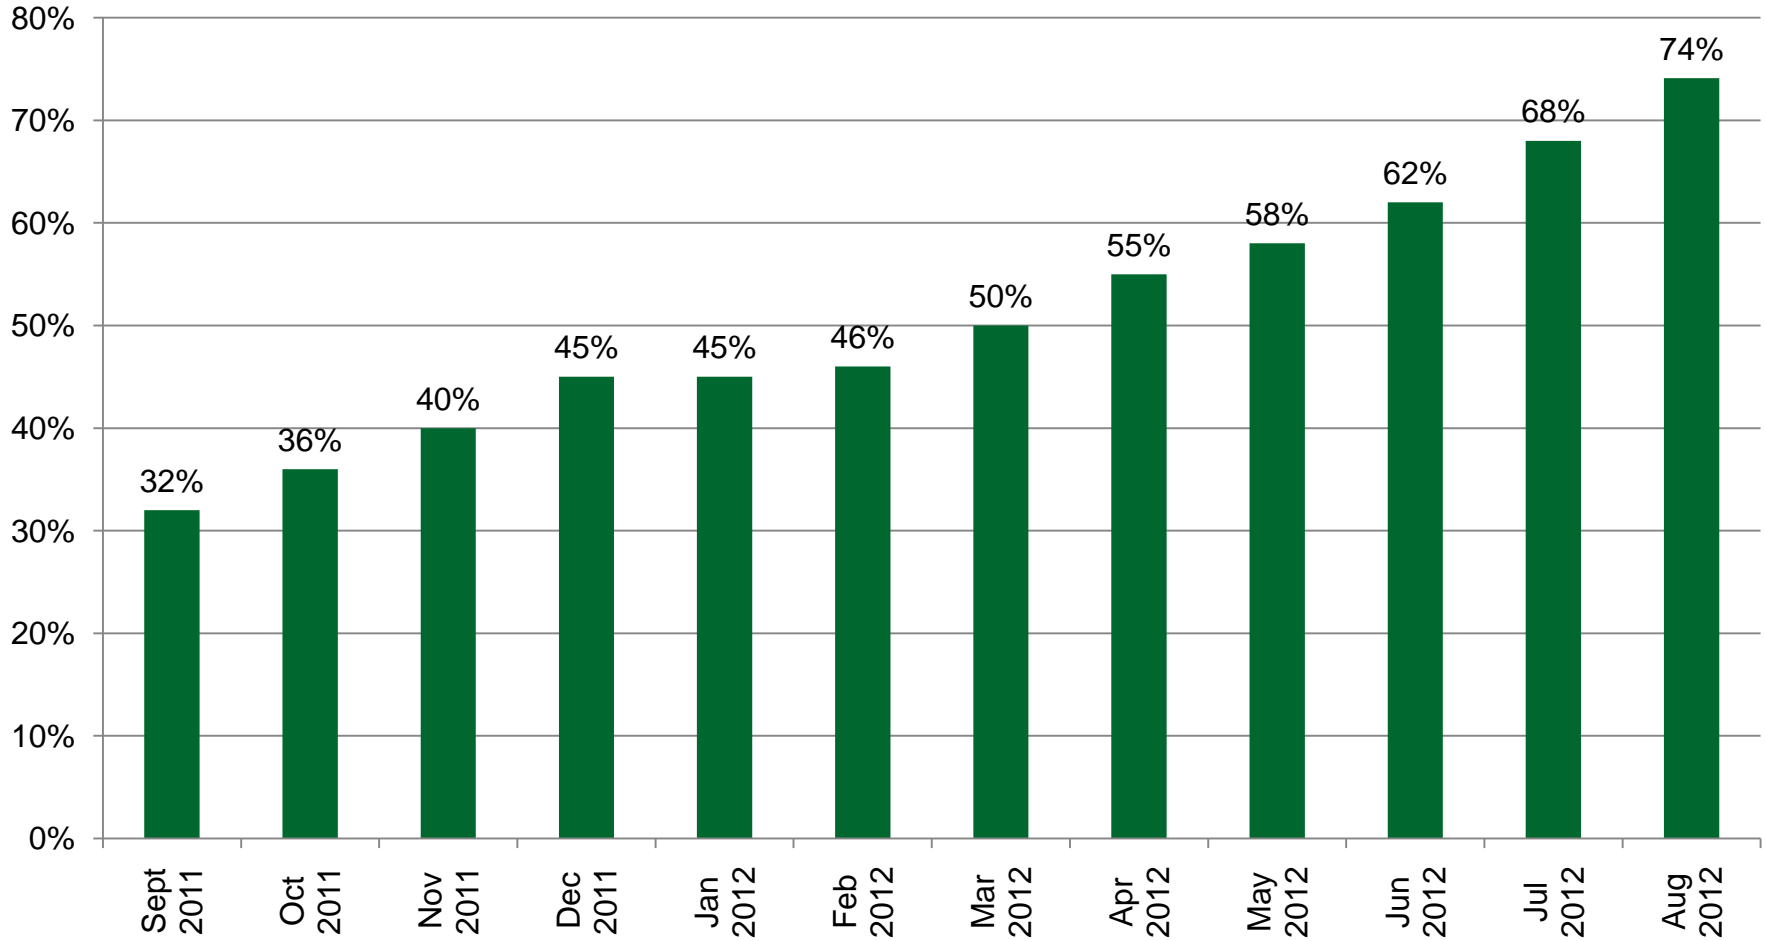

# Design and Construction Support During Construction



- AECOM providing design and construction support on five major contracts
  - Civil West
  - Civil East
  - Operations and Maintenance Facility
  - Systems
  - Light Rail Vehicles Procurement

# Civil West Construction Status

- Substantial Completion expected in late 2012
- Final contract completion activities will carry into 2013

*Civil West: FST Tub Near East Bank Station*



# Civil East Construction Status

- Substantial Completion expected in mid 2013
- Final contract completion activities into late 2013

*Civil East: University Avenue at Pillsbury*





# Operations and Maint. Facility Status



- Substantial Completion of the building expected in Q2 2013
- Substantial Completion of the balance of the contract, including yard, expected in late 2013

*OMF: Entry Lobby Drywall Framing*

# Systems Status

- Contract activities to peak in 2013
- Significant contract work, including systemwide testing, will be on-going throughout 2013

*Systems: OCS Wide Flange Pole Set*



# Light Rail Vehicle Status

- First two vehicles delivered and testing underway
- More than 40 vehicles will be delivered by end of 2013

*#201 Dynamic Testing in the Tunnel*



# Other Design/ Construction Contracts in 2013



- Washington Avenue Bridge Lighting
- Cedar Riverside Intersection Improvements
- Art Contracts Installation
- Ford Building Areaway Design and Construction

# Recommendation

Authorize the Regional Administrator to negotiate and execute an amendment to:

- Increase AECOM contract value by \$7.0 million to \$112.2 million
- Issue additional work orders for 2013 for overall spending authority not-to-exceed \$111.7 million

# More Information



Check out our website:

- [www.centralcorridor.org](http://www.centralcorridor.org)

Contact Central Corridor Project  
Office:

- 540 Fairview Avenue North  
St. Paul, MN 55104
- Construction Hotline: 651-602-1404
- Comment Line: 651-602-1645
- Email:  
[centralcorridor@metc.state.mn.us](mailto:centralcorridor@metc.state.mn.us)
